

August 18, 2021

Dear Property Owners:

**Re: Project Notification – Cabana Road Corridor Improvements Phase 3 –  
Road Widening, Storm Sewer and Watermain – Interim Notice**

---

Further to our notice of project commencement dated April 9, 2021, we would like to update you on the work completed to date, anticipated next steps and project milestones.

**Work Completed to Date**

- Watermain and services from Northway to Dougall
- Temporary lanes and traffic signals to facilitate construction
- Storm sewer and services from Mt. Carmel to Dougall are largely complete
- Road construction along the south side of Cabana from Mt. Carmel to Dougall is well underway
- Reconstruction of the Dominion/Mt. Royal intersection with Cabana Road is also well underway

**Anticipated Next Steps**

- Traffic will be shifted completely to the north side of Cabana by August 18<sup>th</sup>
- Completion of the storm sewer mainline and south private drain connections by August 27<sup>th</sup>
- Completion of the roadwork along the south side of Cabana including curbs, sidewalks, street lights and asphalt paving will continue until late September.
- Once the south side of Cabana is complete, traffic will be moved to the south side and road construction will commence along the north side of Cabana. Restoration and landscaping along the south side of Cabana will still be on-going.
- Improvements to the Dougall / Cabana intersection will be completed in the fall.

## Project Milestones

- The Contractor is working diligently to see the Dominion/Mt. Royal intersection with Cabana open before the start of school on September 7<sup>th</sup>.
- It is anticipated that construction will commence on the north side of Cabana Road by the last week in September.
- It is anticipated that construction will be substantially complete by early December 2021
- Surface asphalt paving and related works will be completed in the spring of 2022.

We understand that construction can cause inconveniences to the adjacent residents including driveway access, deliveries, taxi services, garbage collection, etc. **If assistance is required please contact Samuel Klomp of Amico Infrastructures at 519-999-0747. He will arrange for onsite staff to provide assistance.**

We appreciate your understanding and cooperation on this matter. We will continue to communicate with you as the project progresses to completion. Should you have any questions or concerns related to this project, please contact:

Jane He, P. Eng.  
Project Manager  
City of Windsor Engineering Department  
(519) 255-6100 ext. 6358

Tina Hawco, P. Eng.  
Project Engineer  
Dillion Consulting Limited  
(519) 948-5000, extension 3274


Yours truly,



Fahd Mikhael, P. Eng., P.E., M. Sc  
Manager of Design and Development

Attachments: Map of Location of the Work

cc: Amico Infrastructures Inc., Attn: Jeff Rahm, Samuel Klomp  
Ward 1 Councillor Fred Francis  
311, Attn: Marianna Mosceo

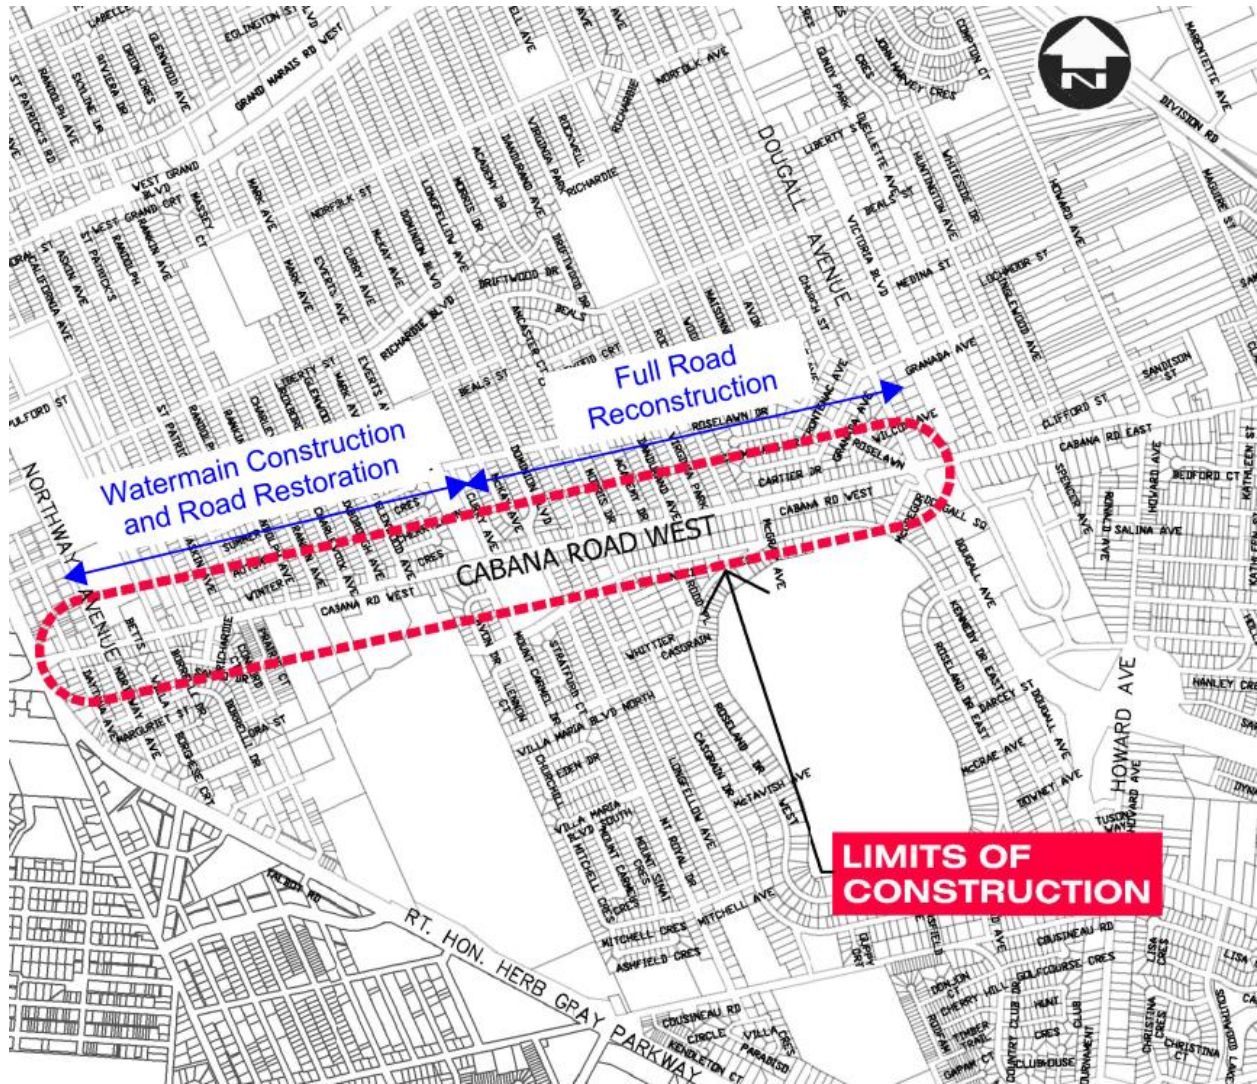

### Cabana Corridor Improvements – Phase 3 Location of Work
